





Stage 2 LRT Update January 2023 7pm




# Ottawa Blair Station Connecting Stage 1 to Stage 2




















## Jeanne d'Arc Station

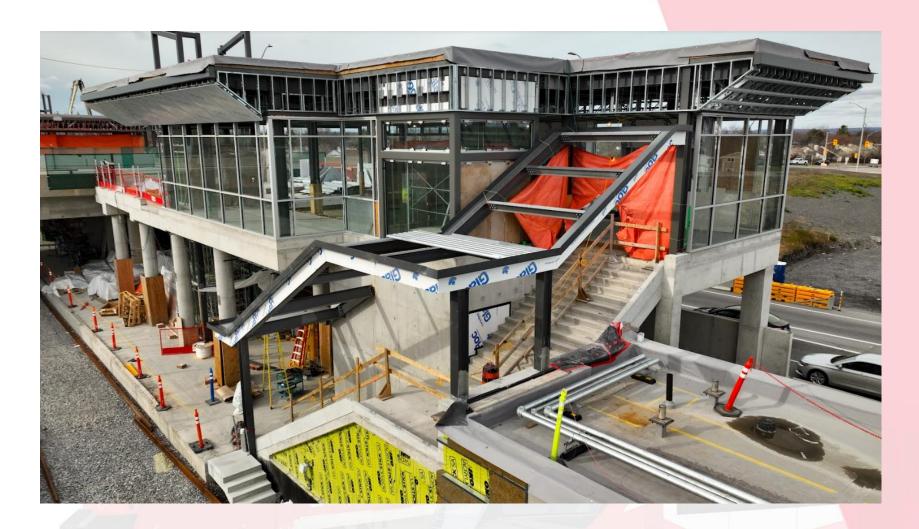







#### Jeanne d'Arc Blvd










## Jeanne d'Arc Blvd: Cross Section

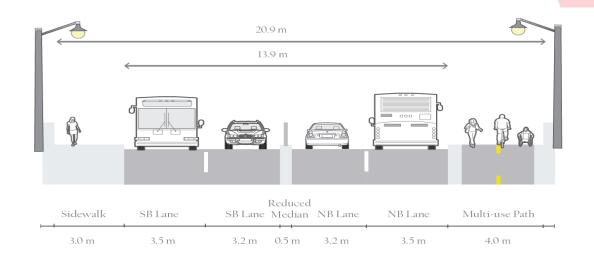







## Convent Glen Station










## Orléans Blvd Overpass

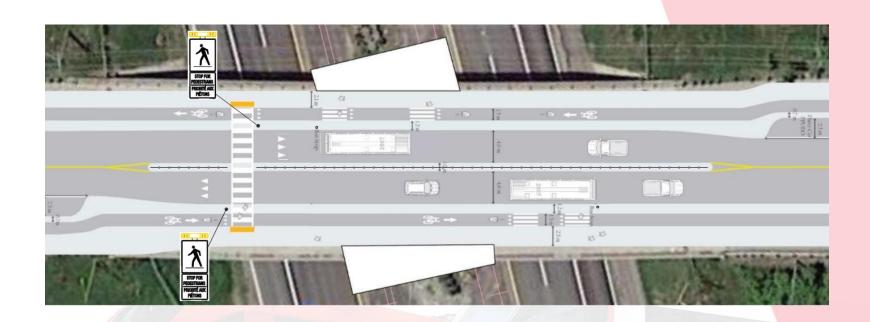







## Place d'Orléans Station









## Place d'Orléans Connectivity










## **Trim Station**

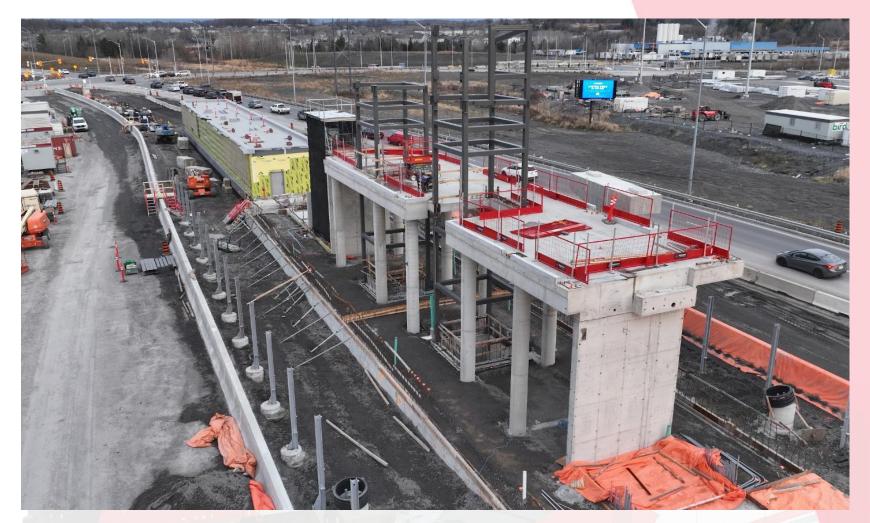







## Pedestrian Bridges in the East









## Noise Walls - North Side

Noise Wall	Ward	Location	Status
B01	11	OR 174 west of Montreal Road Station	Complete.
B02	2	OR 174 between Jeanne d'Arc and Orleans Blvd	In 2023, the wall will be extended further west toward the Jeanne d'Arc Blvd off ramp.
B03	2	OR 174 between Orleans Blvd and Bilberry Creek	Complete.
B04	2	OR 174 between Bilberry Creek and the Place d'Orleans North Park & Ride	Completion of this wall is taking longer than initially estimated due to very hard bedrock and limited site access. Installation of the noise wall posts is complete, and the construction of a retaining wall is well underway. In early 2023, crews will complete the construction of the retaining wall, followed by the installation of the noise wall panels.
B05	1	OR 174 between Champlain St and Tenth Line	Complete.







## Noise Walls - South Side

Noise Wall	Ward	Location	Status
B06	2	South side of the OR 174 between Jeanne d'Arc Blvd and Orleans Blvd	Preparatory work occurred in 2022. Construction is expected to commence in 2023.
B07	2	South side of the OR 174 between Orleans Blvd and Stoneboat Cres, terminating at Stoneboat Park	Preparatory work occurred in 2022. Construction is expected to commence in 2023.
B08	2	South side of the OR 174 beginning at Cholette Cres pathway heading east towards Bilberry Creek	The proposed location of the wall conflicts with existing utility infrastructure. As a result, this section of the wall had to be descoped from the project.
B09	1	South side of the OR 174 at Terra Nova Estates	10% complete, work is expected to continue into 2023.







## Noise Wall B07 and B08









## North Side Noise Wall









#### Communication Resources Available:

#### Ottawa.ca/stage2 for:

- Project updates
- Traffic impacts
- Sign up for station specific email newsletter

Email: stage2@ottawa.ca

Weekly overnight impacts sent Mondays

Social media:

Instagram: @stage2etape2







## Merci / Thank You



